

LOCATION 4206 Beatty Rd CITY GASTONIA
BETWEEN Tebby Rd STREET & Cove Creek STREET

	SIZE	TYPE	LENGTH	INSTALLED	RETIRED	RENEWED
MAIN TO BLDG.	<u>3/4'</u>	<u>Plastic</u>	<u>77'</u>	<u>5/24/95</u>		
MAIN TO PROP. LINE	<u>3/4'</u>		<u>12'</u>			
PROP. LINE TO BLDG.	<u>3/4'</u>		<u>65'</u>			

ENTERS: 4206 BRANCHED INTO:
TAP SIZE: 3/8" PRESSURE 60 P.S.I. _____ INCHES W.C. LOCATION West side of 4206


PRESSURE TEST: @ 100 psi For 1/4 Hrs. By DT

MAIN-SIZE 6" C.I. _____ BARE STEEL _____ COATED STEEL ☒ PLASTIC _____ YEAR INSTALLED 1995

DEPTH: 3 Ft. 0 In. LOCATION East side of Beatty Rd

"A" P/S READING 1.20 TOTAL ANODES 1# 0 17# 0 L.R. # 233120

REMARKS:

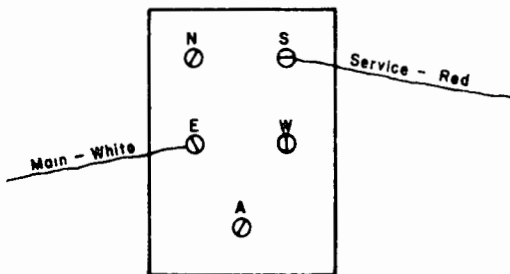

Test Station		
Reading & Location	Lead	Volts
P/S Pipeline Lead - Red New Service	S	
P/S Pipeline Lead - White Existing Main	E	

ENG. DEPT. USE ONLY
